Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Schedule % Complete
City of Maple Grove - Wellington Crest Street Reh		76	02-Jun-16 A	16-Sep-16	0	0%
PHASE 1		30	02-Jun-16 A	07-Jul-16	4	0%
A1020	Adjust (Lower) Castings & Gate Valves	3	02-Jun-16 A	06-Jun-16	1	66.67%
A1010	Install Traffic Control	1	06-Jun-16	06-Jun-16	1	0%
A1030	Reclaim Streets	2	06-Jun-16	07-Jun-16	0	0%
A1040	Remove Curb & Driveways	4	06-Jun-16	09-Jun-16	0	0%
A1005	Install Erosian Control	1	06-Jun-16	06-Jun-16	1	0%
A1050	Install Strom Sewer Pipe & Structures	2	06-Jun-16	07-Jun-16	0	0%
A1055	Instrall 6" PVC Pipe & Perforated Pipe	2	08-Jun-16	09-Jun-16	0	0%
A1060	Grade & Proof Roll Streets (Wellington)	2	10-Jun-16	13-Jun-16	0	0%
A1070	Grade, Proof Roll and Correct Centerline Streets (Pineview)	2	14-Jun-16	15-Jun-16	0	0%
A1080	Install New Crub & Gutter	2	16-Jun-16	17-Jun-16	0	0%
A1090	Install Driveways & Sidewalk	4	20-Jun-16	23-Jun-16	0	0%
A1110	Fine Grade Streets	3	20-Jun-16	22-Jun-16	0	0%
A1120	Install First Lift Bituminous Pavement	2	23-Jun-16	24-Jun-16	0	0%
A1100	Backfill Curb & Sidewalk	1	24-Jun-16	24-Jun-16	0	0%
A1130	Install Topsoil	3	27-Jun-16	29-Jun-16	0	0%
A1125	Install Interim Pavement Markings	1	27-Jun-16	27-Jun-16	0	0%
A1140	Turf Establishment	2	30-Jun-16	01-Jul-16	0	0%
A1150	Final Lift Asphalt Pavement	2	05-Jul-16	06-Jul-16	0	0%
A1155	Install Final Markings	1	07-Jul-16	07-Jul-16	0	0%
A1004	Phase 1 Completion	0		07-Jul-16*	5	0%
PHASE 2		26	07-Jul-16	05-Aug-16	0	0%
A1350	Install Traffic Control	1	07-Jul-16	07-Jul-16	0	0%
A1360	Adjust (Lower) Castings & Gate Valves	2	07-Jul-16	08-Jul-16	0	0%
A1340	Install Erosian Control	1	07-Jul-16	07-Jul-16	0	0%
A1370	Reclaim Streets	1	08-Jul-16	08-Jul-16	0	0%
A1380	Remove Curb & Driveways	3	08-Jul-16	12-Jul-16	0	0%
A1400	Instrall 6" PVC Pipe & Perforated Pipe	3	08-Jul-16	12-Jul-16	0	0%
A1410	Grade & Proof Roll Streets (Subdivison)	3	13-Jul-16	15-Jul-16	0	0%
A1430	Install New Crub & Gutter	3	18-Jul-16	20-Jul-16	0	0%
A1440	Install Driveways	5	19-Jul-16	25-Jul-16	1	0%
A1435	Curb & Gutter Spot Replacments	2	19-Jul-16	20-Jul-16	1	0%
A1460	Fine Grade Streets	3	21-Jul-16	25-Jul-16	0	0%
A1450	Backfill Curb	2	22-Jul-16	25-Jul-16	1	0%
A1470	Install First Lift Bituminous Pavement	1	26-Jul-16	26-Jul-16	0	0%
A1490	Install Topsoil	3	27-Jul-16	29-Jul-16	0	0%
A1500	Turf Establishment	2	01-Aug-16	02-Aug-16	0	0%
A1505	Edge Mill Exsisting Streets	1	03-Aug-16	03-Aug-16	0	0%
A1510	Place 1.5" Overlay	1	04-Aug-16	04-Aug-16	0	0%
A1515	Final Lift Asphalt Pavement	1	05-Aug-16	05-Aug-16	0	0%
A1339	Phase 2 Completion	0		05-Aug-16*	0	0%
PHASE 3		20	08-Aug-16	02-Sep-16	0	0%
A1170	Install Traffic Control	1	08-Aug-16	08-Aug-16	0	0%
A1180	Adjust (Lower) Castings & Gate Valves	3	08-Aug-16	10-Aug-16	0	0%
A1160	Install Erosian Control	1	08-Aug-16	08-Aug-16	0	0%

Actual Work | Critical Remaining Work | Summary | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Schedule % Complete
A1190	Reclaim Streets	1	10-Aug-16	10-Aug-16	0	0%
A1220	Instrall 6" PVC Pipe & Perforated Pipe	3	10-Aug-16	12-Aug-16	0	0%
A1200	Remove Curb & Driveways	2	11-Aug-16	12-Aug-16	0	0%
A1230	Grade & Proof Roll Streets (Subdivision)	3	15-Aug-16	17-Aug-16	0	0%
A1250	Install New Crub & Gutter	3	18-Aug-16	22-Aug-16	0	0%
A1260	Install Driveways & Sidewalk	4	23-Aug-16	26-Aug-16	0	0%
A1270	Backfill Curb & Sidewalk	2	23-Aug-16	24-Aug-16	2	0%
A1280	Fine Grade Streets	3	23-Aug-16	25-Aug-16	0	0%
A1290	Install First Lift Bituminous Pavement	1	26-Aug-16	26-Aug-16	0	0%
A1310	Install Topsoil	2	29-Aug-16	30-Aug-16	0	0%
A1320	Turf Establishment	2	31-Aug-16	01-Sep-16	0	0%
A1330	Final Lift Asphalt Pavement	1	02-Sep-16	02-Sep-16	0	0%
A1159	Phase 3 Completion	0		02-Sep-16*	0	0%
Phase 3 Incentive Date		0			0	0%
CLEAN UP		14	03-Sep-16	16-Sep-16	0	0%
A1520	Final Cleanup & Job Closeout	14	03-Sep-16	16-Sep-16	0	0%
A1540	Project Completion Date	0		16-Sep-16*	0	0%

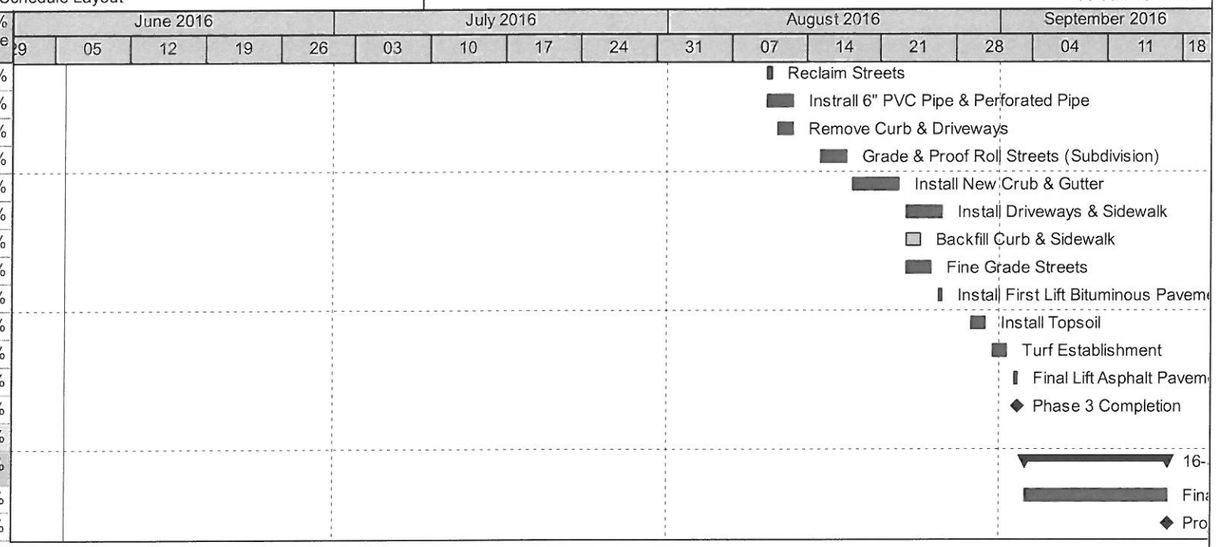

© Oracle Corporation
